



Easier Access Project TTC Greenwood Station

Construction Overview
February 2026

| Status of Easier Access Program



- **64 out of 70** subway stations are accessible with new elevators.
- **6** stations are under construction, including College, Museum, King, Spadina, Islington, and Old Mill.
- **Greenwood Station** has AODA upgrades, including elevators, which were put in service in February 2026. There are other minor works that continue at the station after this date.

| Advisory Committee on Accessible Transit (ACAT)



ACAT Overview

- Toronto citizens who advise the TTC on difficulties faced by people with disabilities and seniors.
- Recommends the elimination of barriers to accessible public transit in the city of Toronto.
- ACAT consists of 15 volunteer committee members who are appointed by the TTC Board.

ACAT's Role

- Represents the needs and concerns of persons with disabilities and seniors who use public transit services provided by the TTC.
- Advises the TTC on the provision of accessible public transit.
- Advises the TTC on necessary policy issues for services that pertain to the interests of persons with disabilities and seniors.
- Supports TTC staff in consulting, educating and advising persons with disabilities, seniors and the community at large.
- Subcommittees: Design Review, Service Planning, Communications, Wheel-Trans Operations.
- Advises the TTC on priority and plans for Easier Access projects.

| Greenwood Station - Easier Access Improvements

TTC made Greenwood Station accessible with new elevators at the existing main entrance building. This work includes:


Barrier-free path from the main entrance to all levels of the station including installation of:

- 2 elevators to access eastbound and westbound platforms
- Automatic sliding station entry doors
- Improved signage
- CCTV – Security cameras along the accessible pathway

The Easier Access improvements are reviewed by ACAT (Advisory Committee on Accessible Transit).

Easier Access Program

- Program to make all stations accessible.
- Elevators, sliding doors, accessible fare gates.
- Elevators are built at the station entrance.

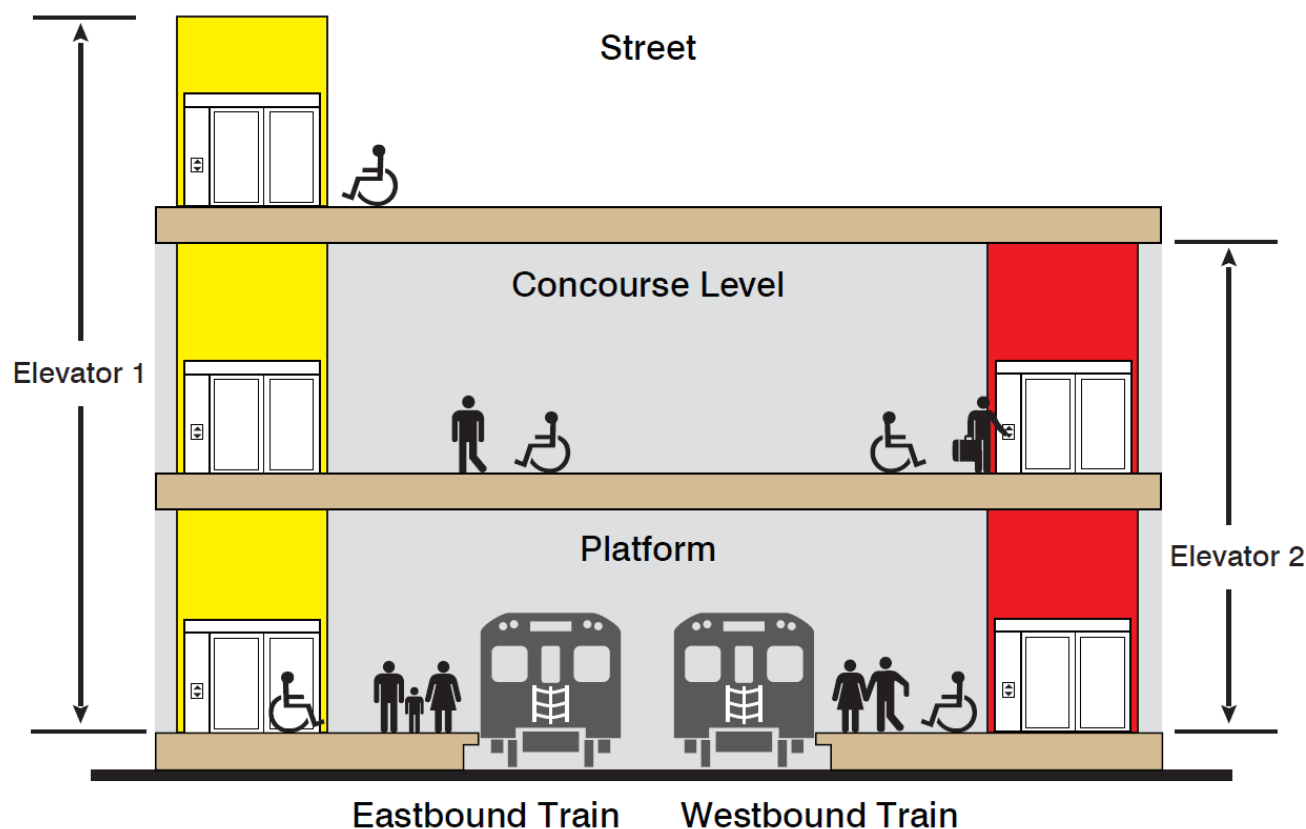

Greenwood Station elevator section image


Greenwood Station Elevator Site Plan



E1 – Street-level location of new elevator to access the street-to-concourse-to eastbound subway platform level.

E2 – Underground location of new elevator to access the concourse-to westbound platform subway level.

Nearby Stations – Accessibility and Construction Schedule

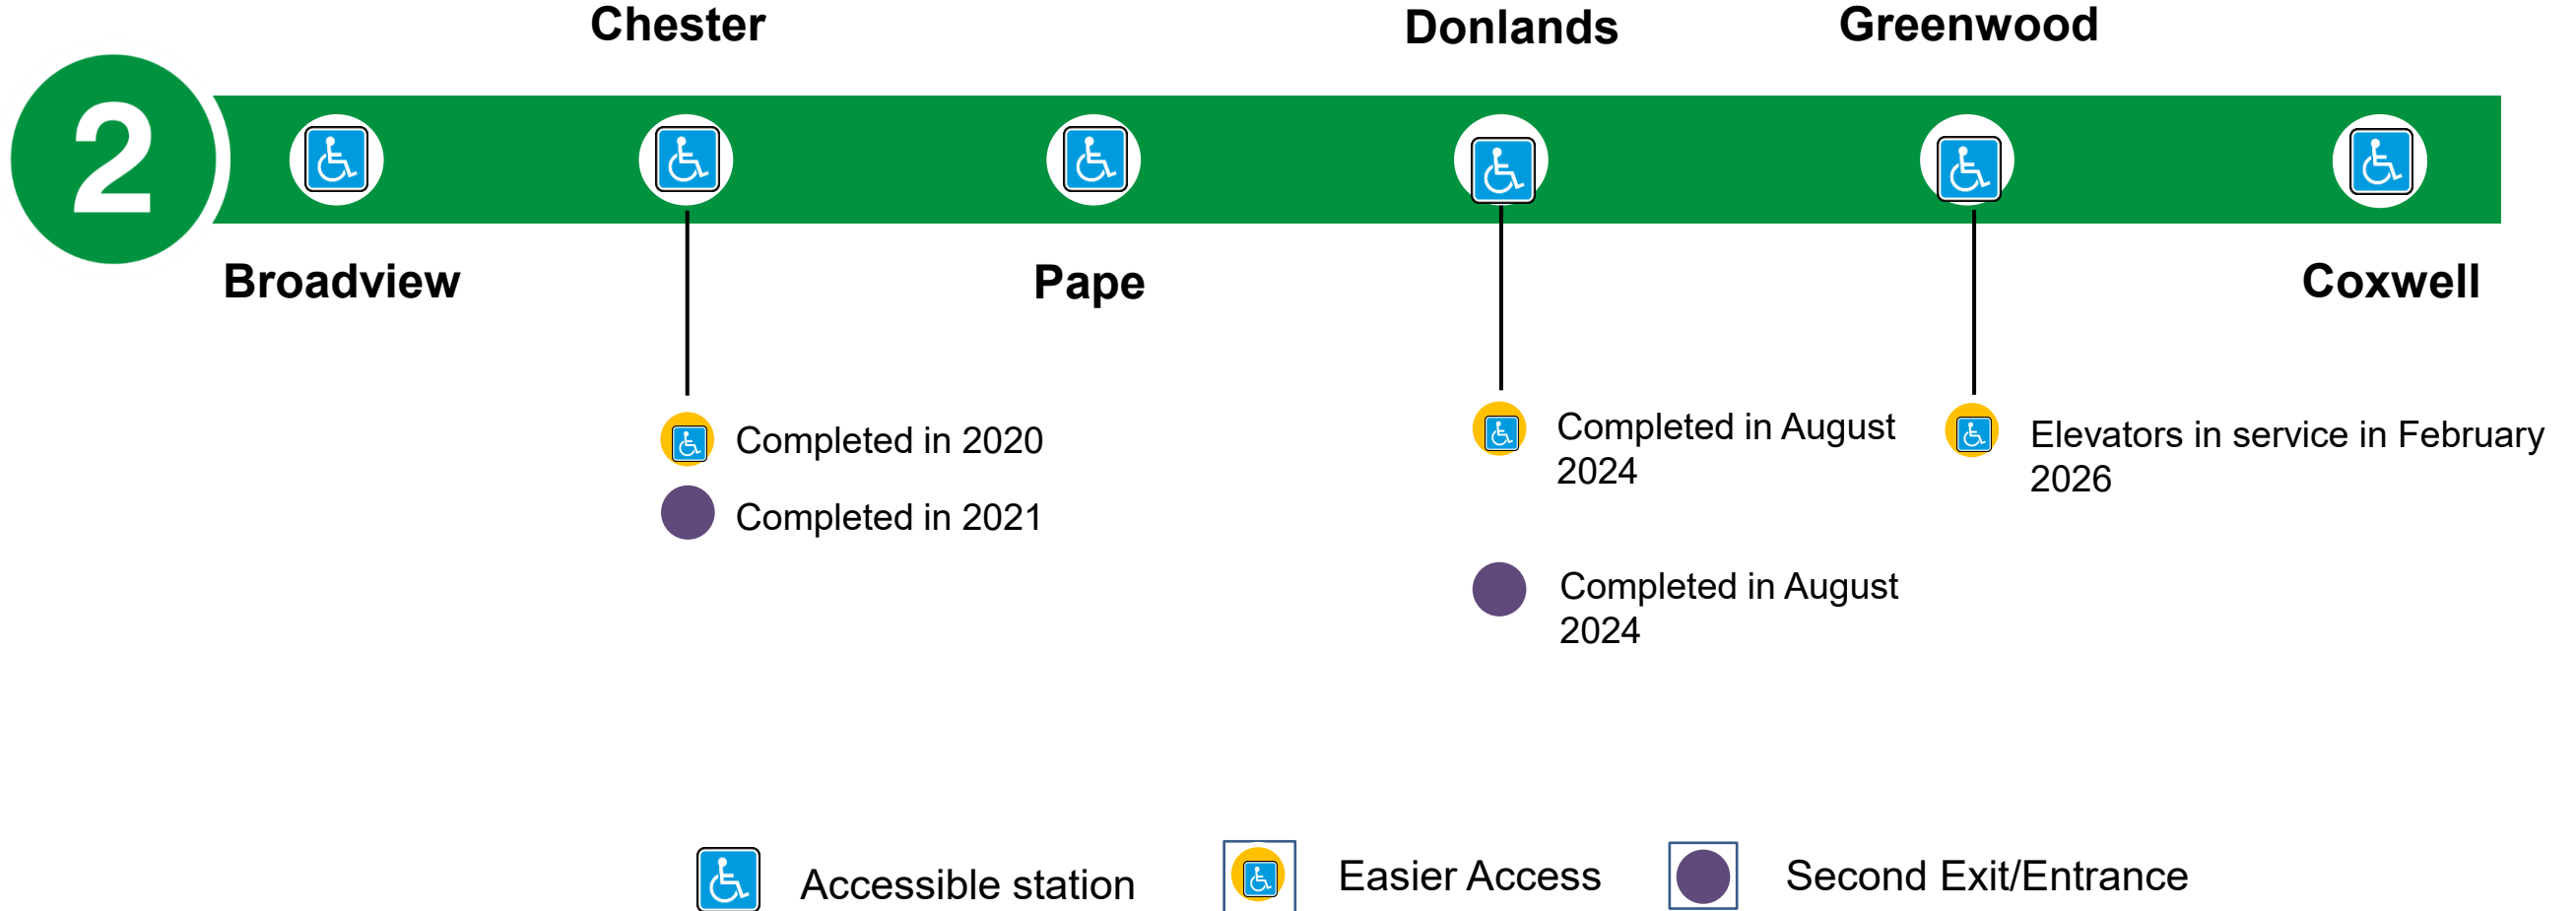

| Greenwood Station Project Schedule

October 7, 2021

Pre-construction community meeting online

Fall 2021

Start construction on elevator project

February 2026

Elevators in service

Summer 2026

Minor works continue after the elevators are in service




| Conceptual Staging Plans

- The following slides include conceptual staging plans - provided for illustrative purposes only.




Conceptual Staging - Phase 1 – Completed in Early 2022

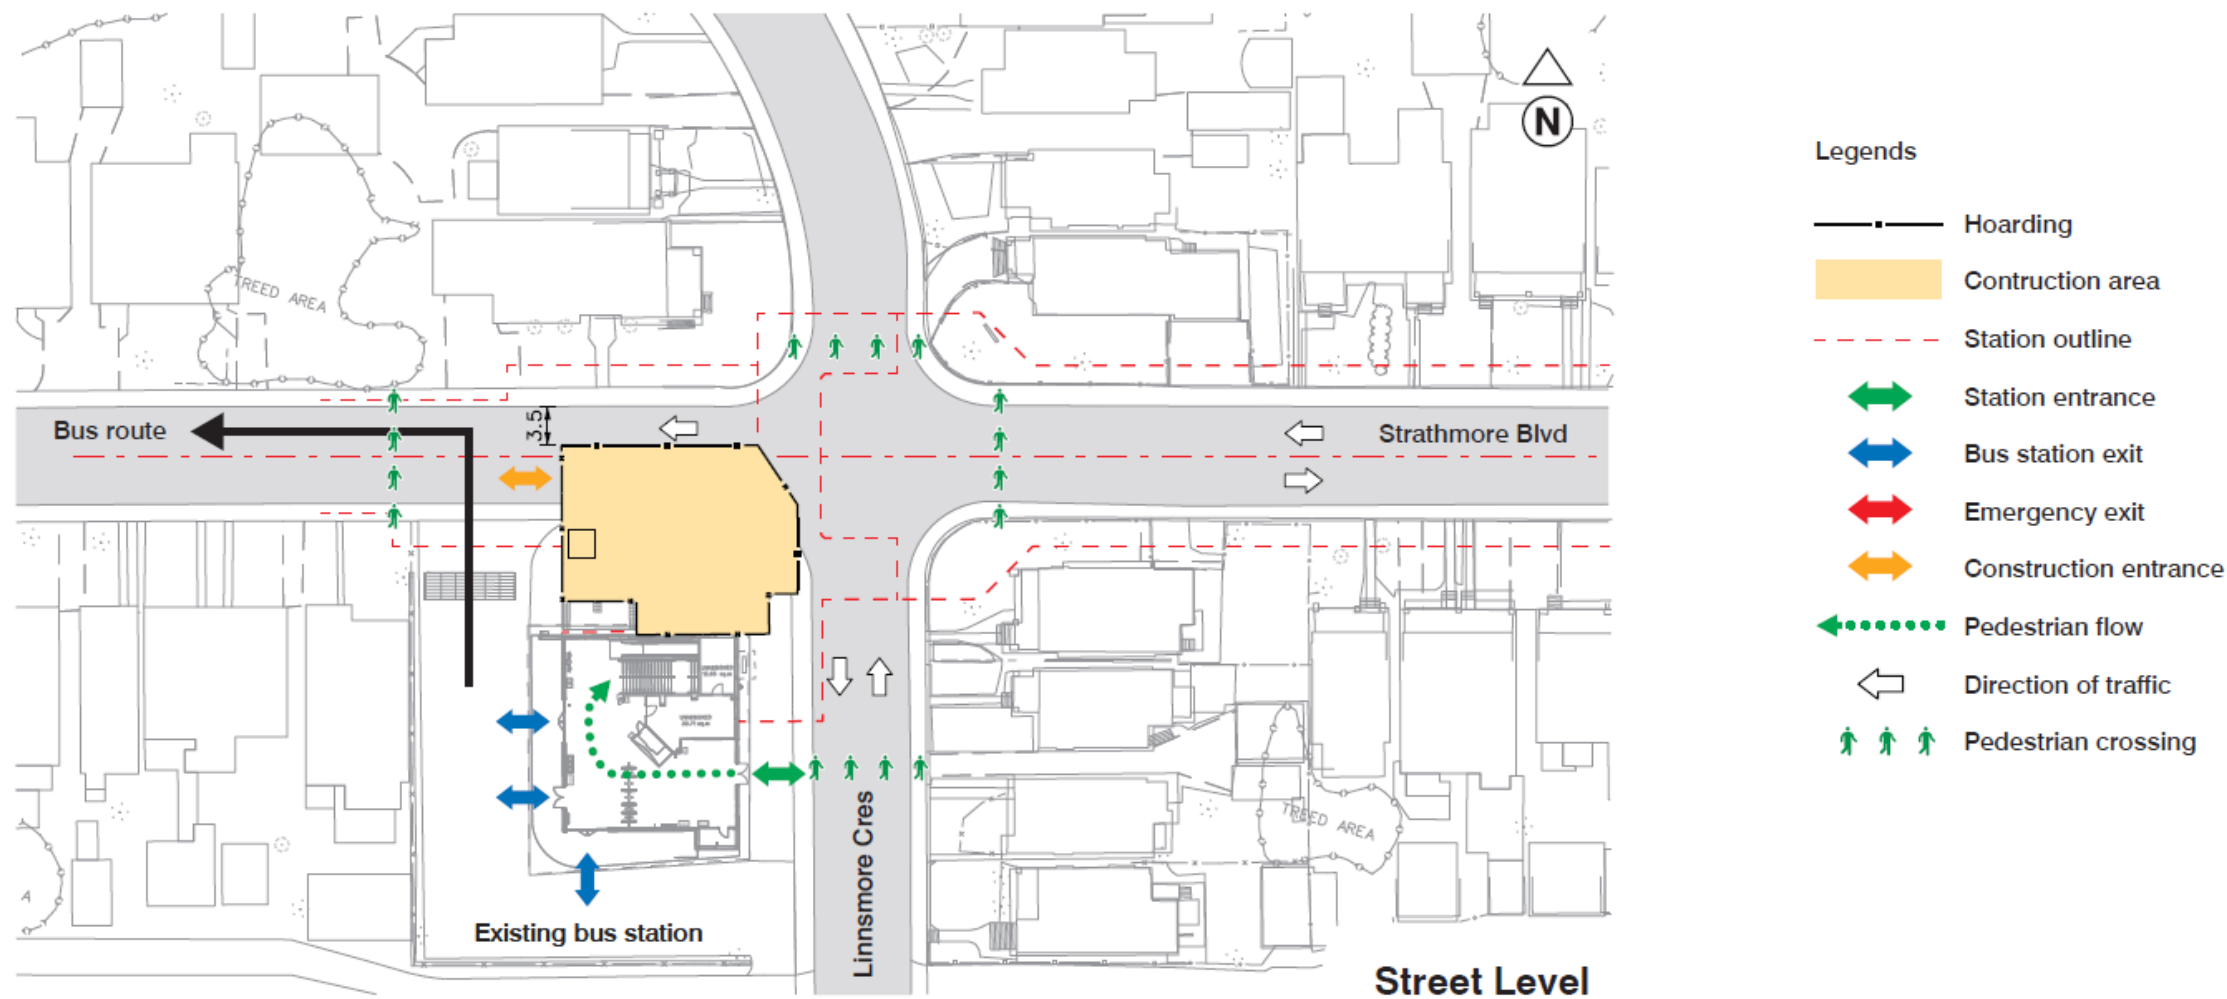


Plans are subject to change

Conceptual Staging - Phase 2 – Completed in 2022

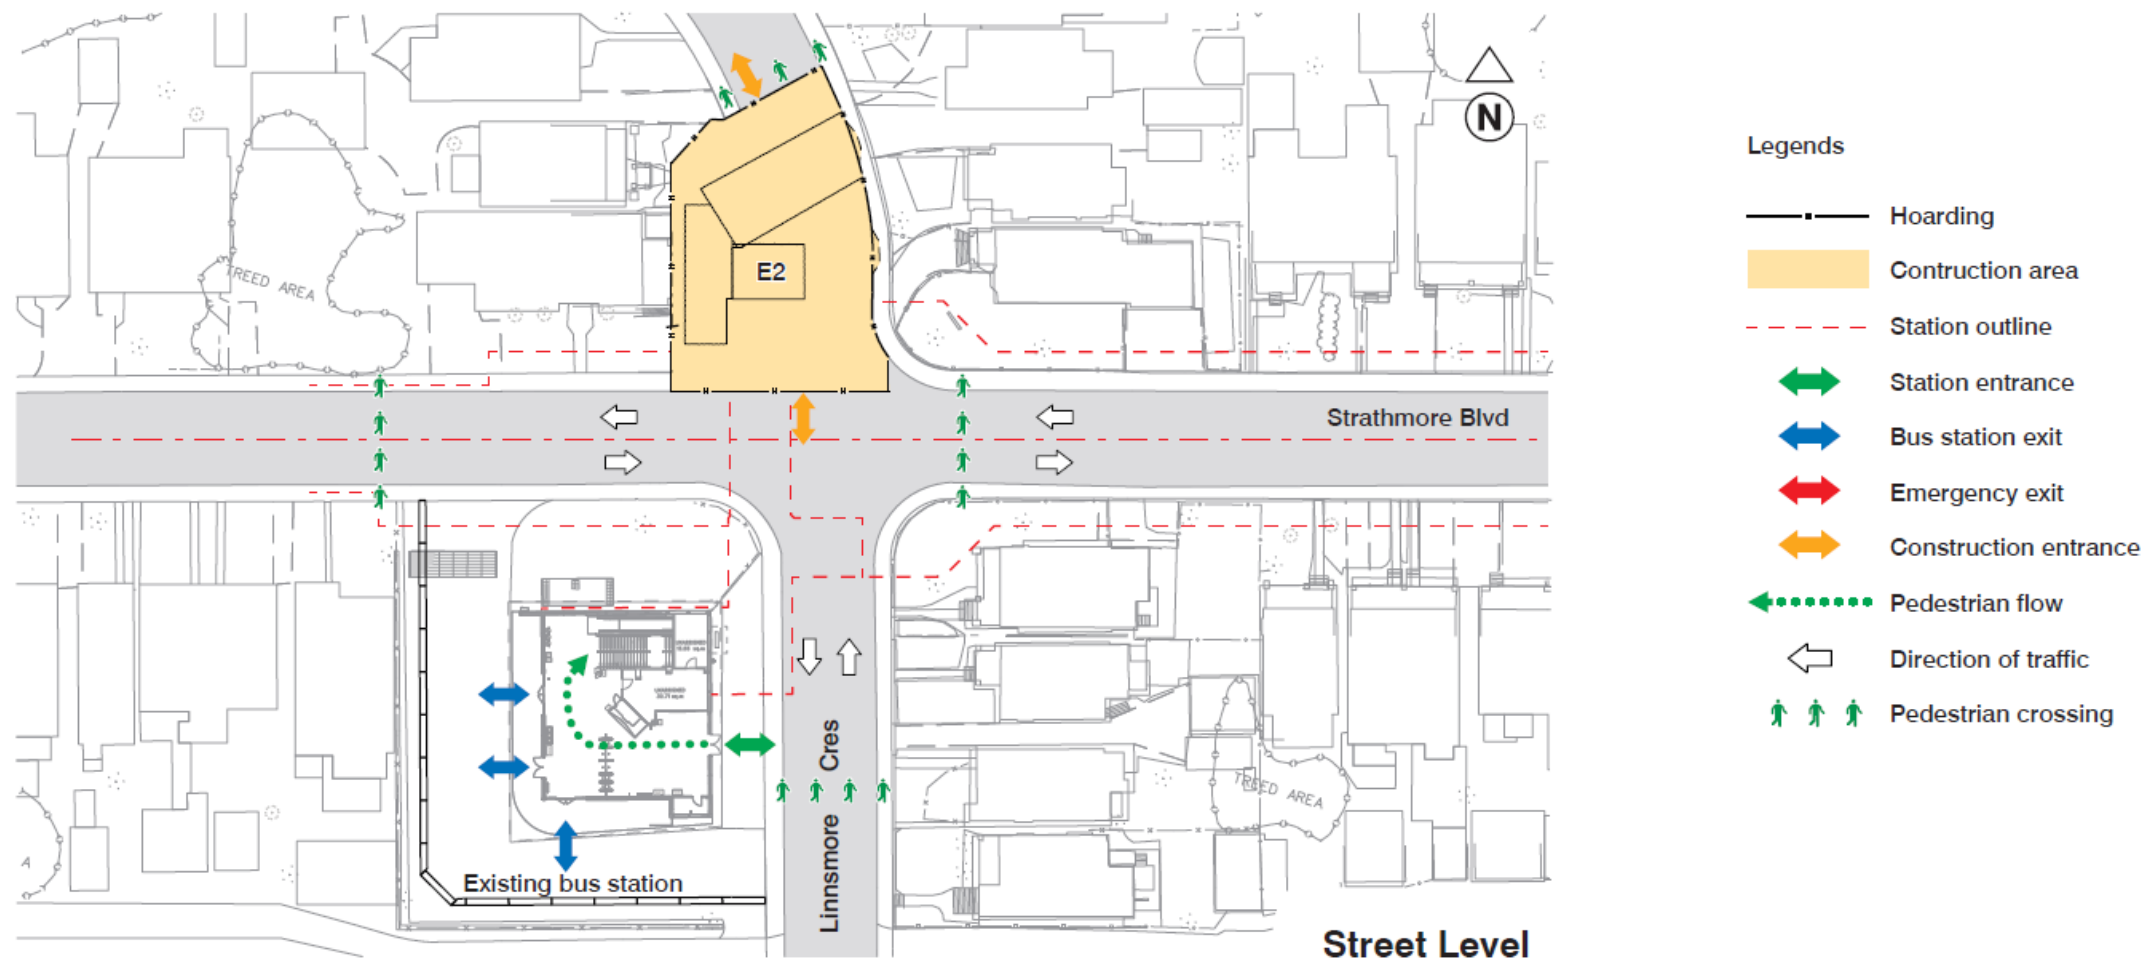


Plans are subject to change

Conceptual Staging - Phase 3 – Completed in Spring 2023

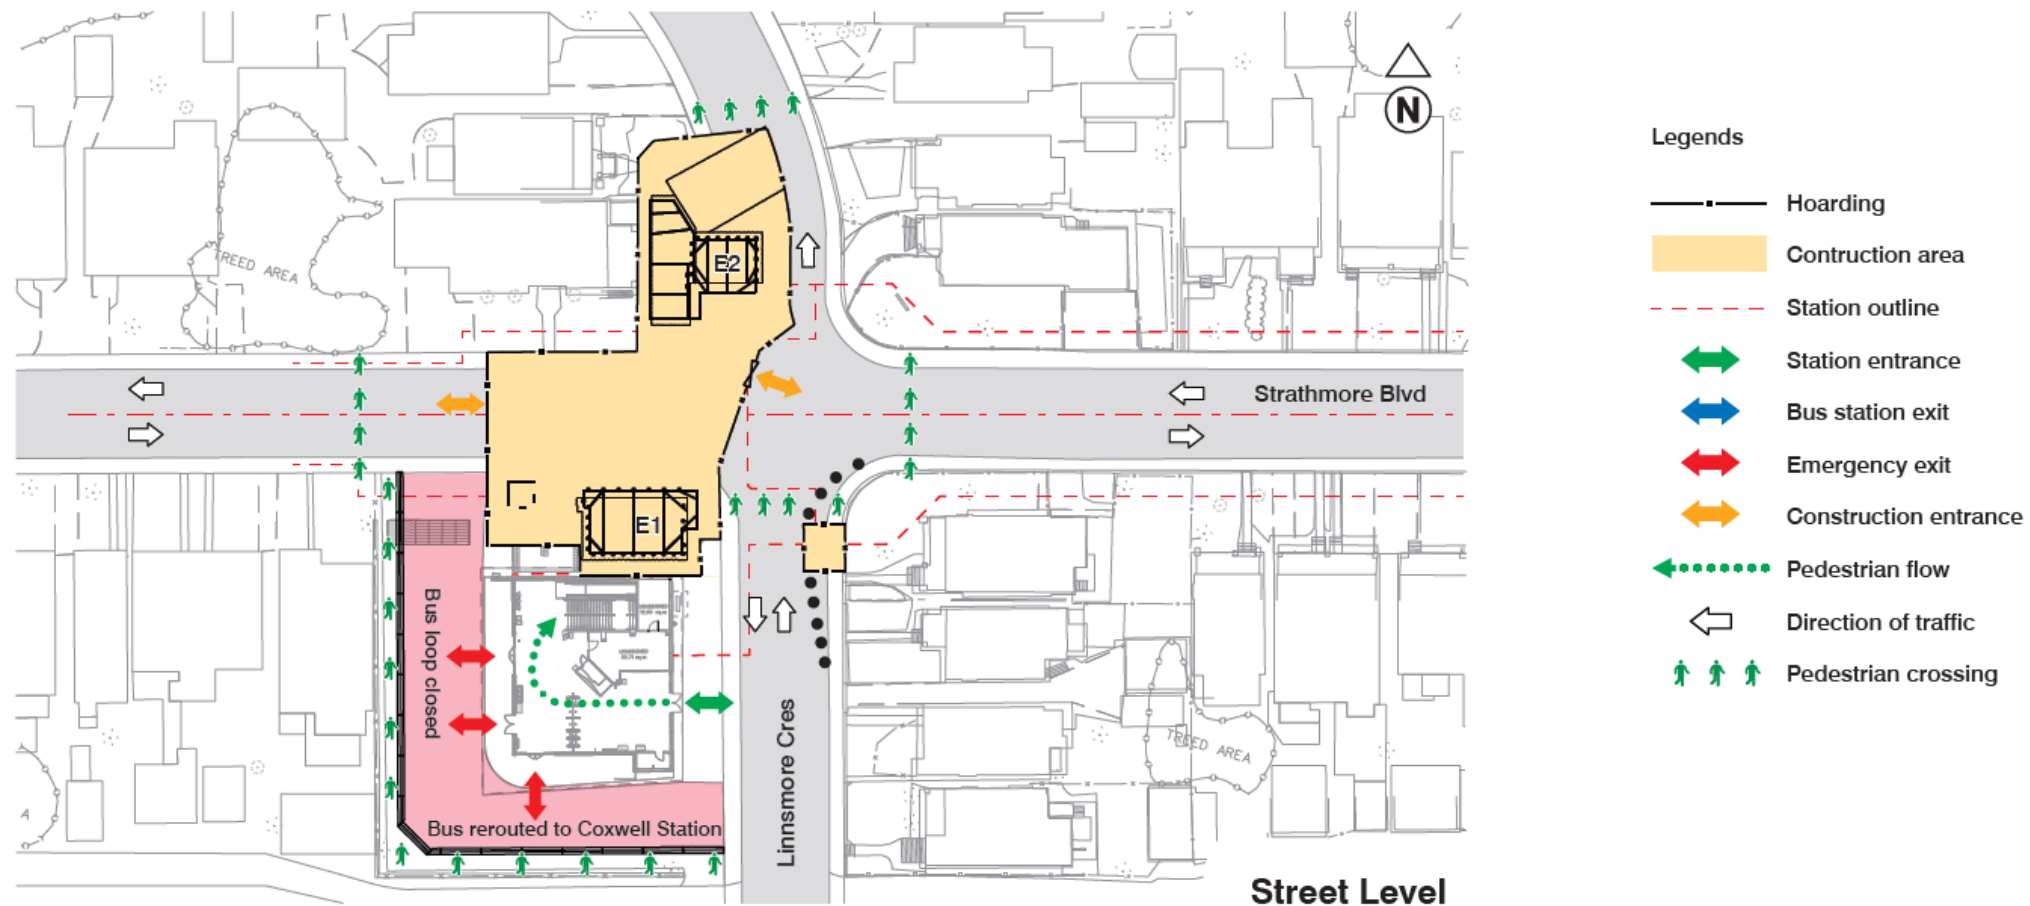


Plans are subject to change

Conceptual Staging - Phase 4 – Completed in Summer 2024

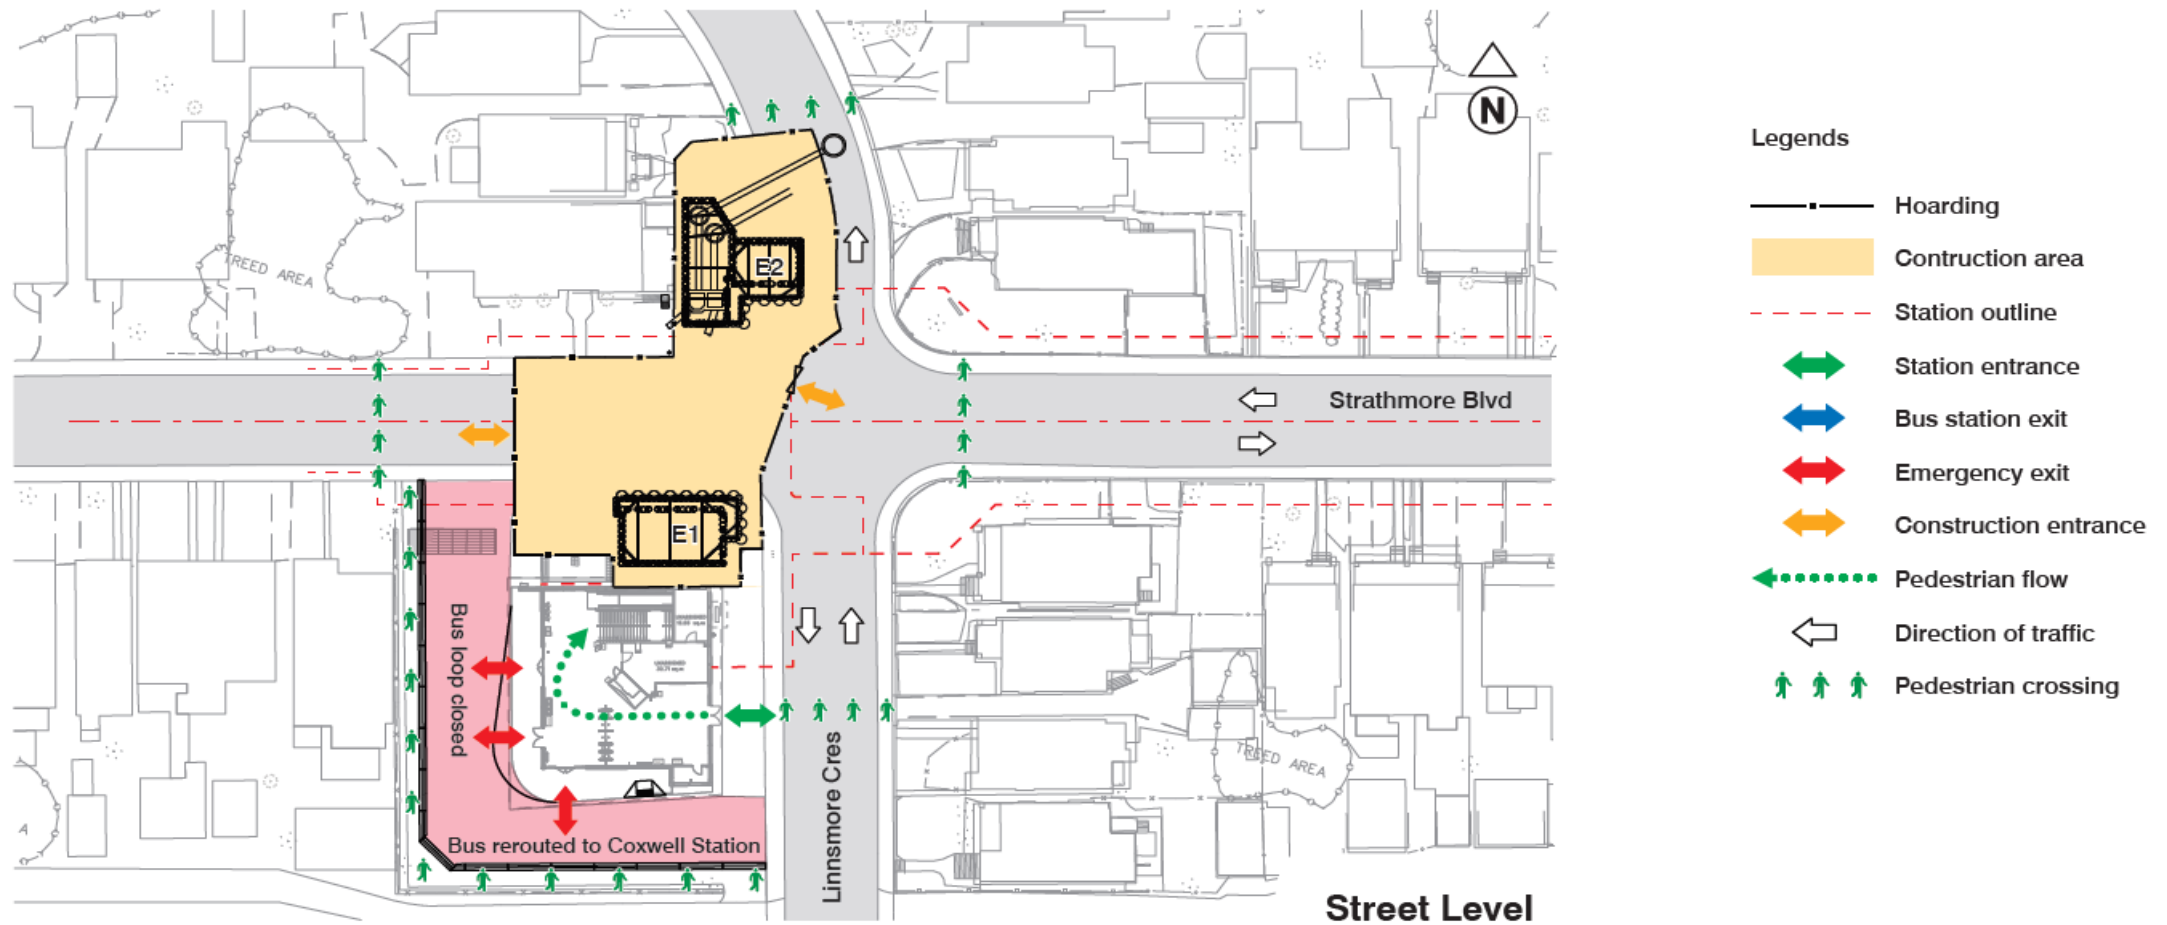

Plans are subject to change


Conceptual Staging - Phase 5 – Completed in December 2024

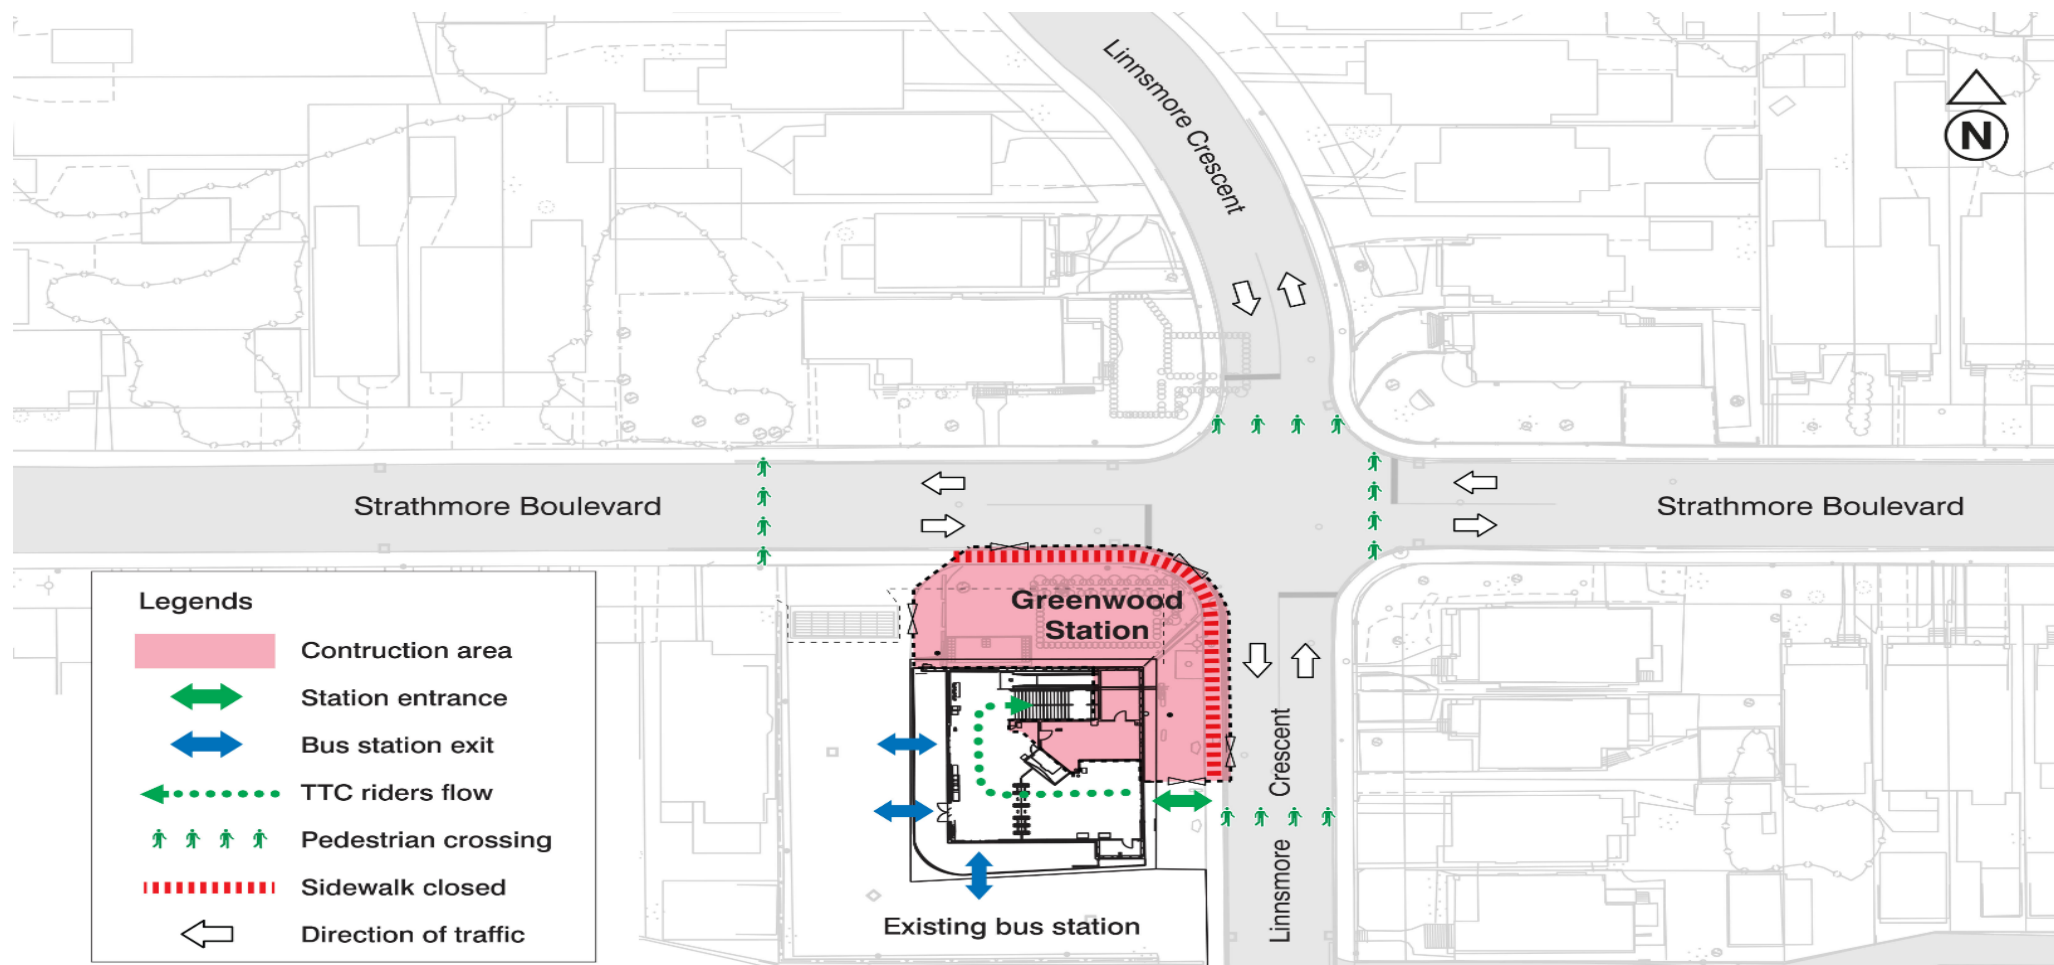

*Pending weather, possible third-party union strikes and unforeseen site conditions and events.

Plans are subject to change

Conceptual Staging - Phase 6 – Estimated Completion in Q1 2026*

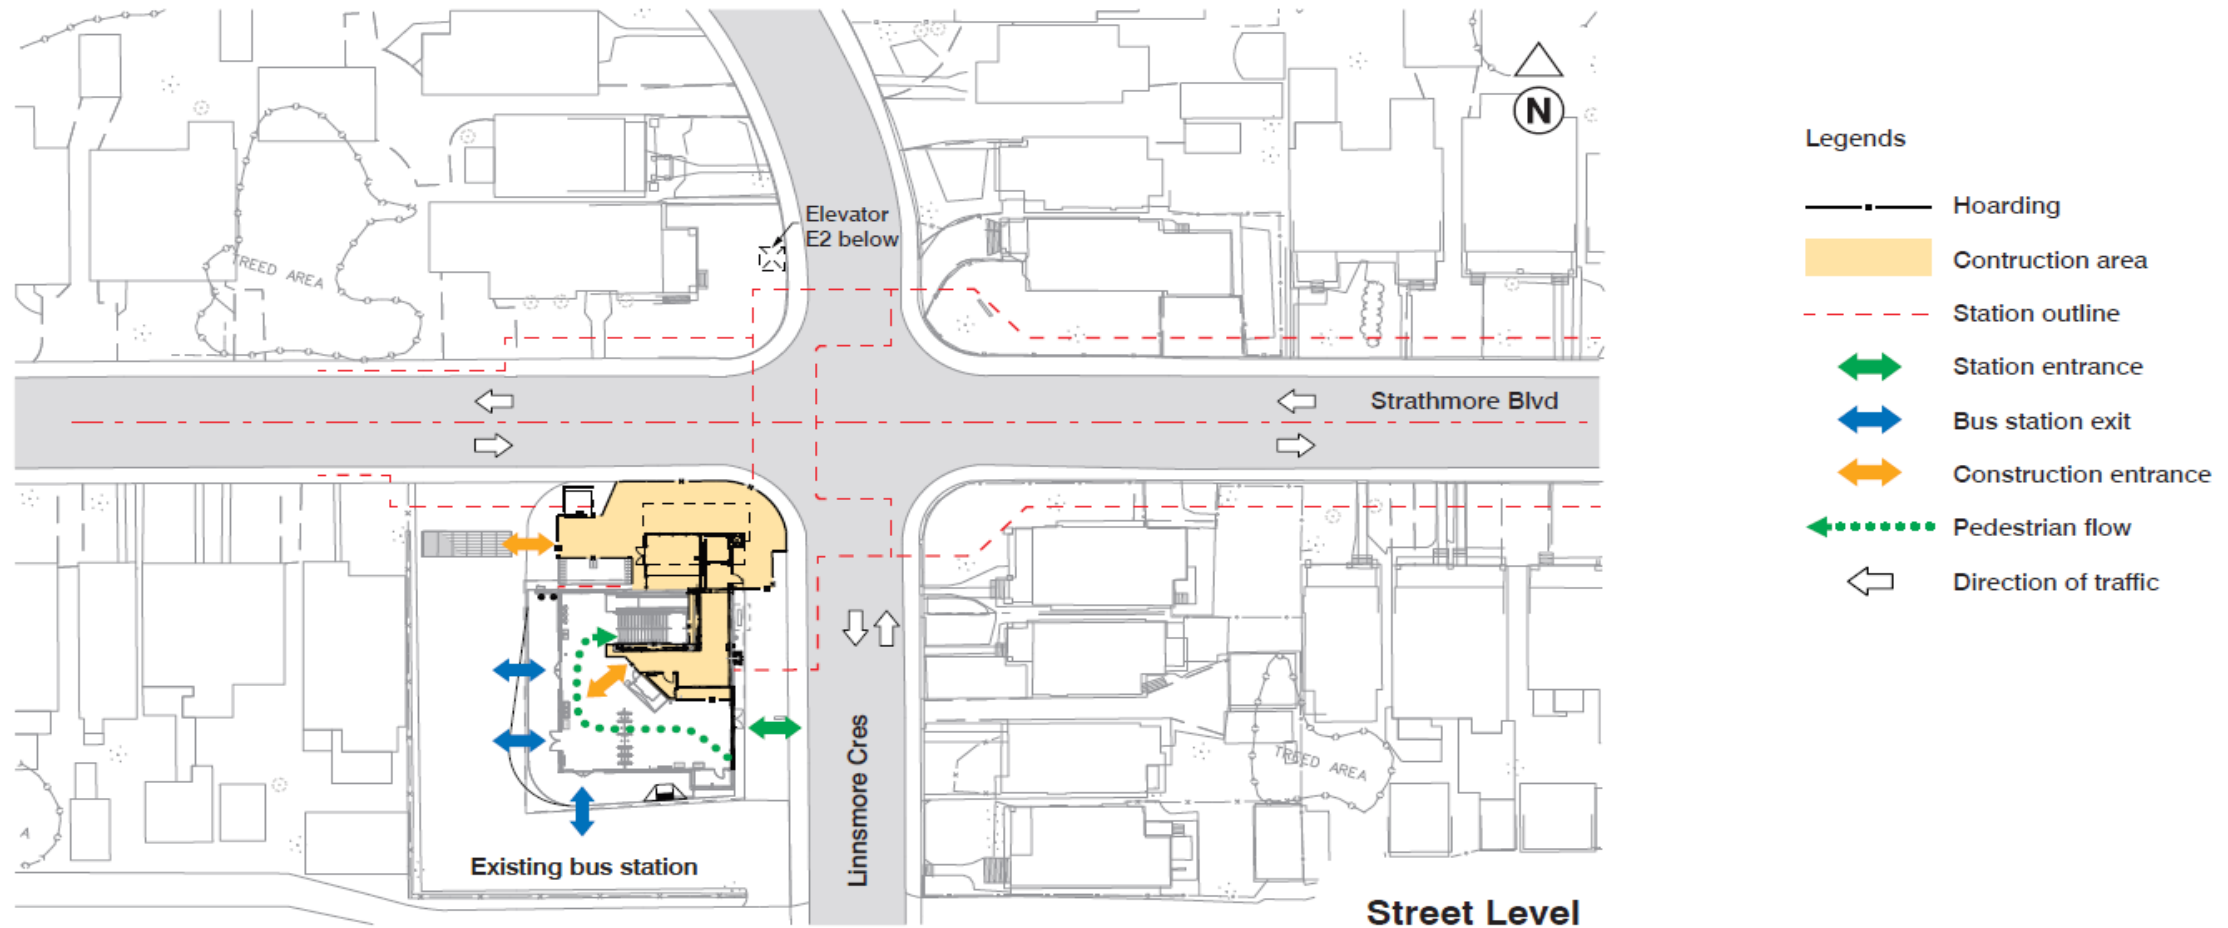

*Pending weather, possible third-party union strikes, and unforeseen site conditions and events.

Plans are subject to change

Construction Progress – Key activities completed and planned for the Easier Access Project

Construction Activity	Status
Stage 1: - Relocation of utilities - Tree removal/protection - Construction hoarding set up - Pedestrian and local traffic detours established	Completed in early 2022
Stage 2: - Linnsmore Cres., at Strathmore Blvd. closed - West sidewalk along Linnsmore Cres., north of Strathmore Blvd. closed to pedestrians - Relocation of utilities	Completed in 2022
Stage 3: - Caisson work ongoing - Bus loop closed at Greenwood Station, the 31 Greenwood buses diverted to Coxwell Station via Danforth Avenue and Coxwell Avenue - Sewer by-pass activities at Linnsmore Cres. Completed	Completed in spring 2023
Stage 4: - Excavation and other activities to build the elevator shafts and associated underground structures - Caisson work continues - Modifications in the interior of the station to accommodate the elevator requirements - Bus loop reopen at Greenwood station. However, 31 Greenwood bus service continues to extend to Coxwell Station to provide an accessible connection for customers requiring the use of elevators. - Strathmore Blvd. restored for vehicular traffic	Completed in summer 2024
Stage 5: - Construction continues underground, on street level, around and within the station building. - Sidewalk re-opened	Completed in December 2024*
Stage 6: - Construction continues underground, on street level, around, and within the station building. - Complete all mechanical and electrical systems related to construction - Removal of hoarding - Restoration and finishing works are ongoing at the station after the elevators are put in service - Elevators in-service	Estimated to be completed in Q1 2026* Elevators in service in February 2026.

*Pending weather, possible third-party union strikes and unforeseen site conditions and events.



| Key Milestones

Key Milestones	Estimated Completion
Elevators in service	February 2026



Construction Photos – February 2026 Progress Update



Photo: Elevator 1 (E1) Platform level - Eastbound



Photo: Elevator 1 (E1) Concourse level - Eastbound

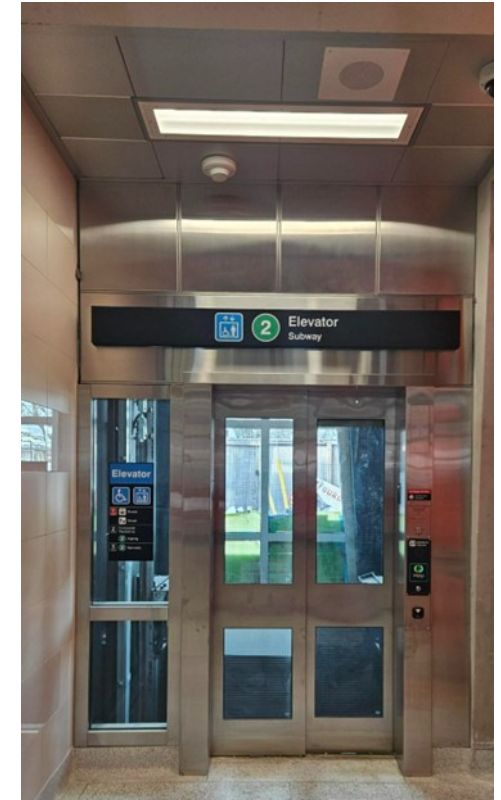


Photo: Elevator 1 (E1) – street level

| Construction Photos - February 2026 Progress Update



Photo: Elevator 2 (E2) Concourse level - Westbound



Photo: Bus loop


| Strathmore & Linnsmore – Parking Impacts

The City of Toronto Transportation has returned Wolverleigh Blvd. parking signs to pre-construction status (i.e., parking on one side of the street at a time). All motorists must abide by the City's posted parking signs.

| Transit Service and Traffic Impacts

- Access to the station will be maintained throughout construction.
- No impacts to subway service on Line 2 – Bloor Danforth.
- During some stages, pedestrian detours will be in place.

Transit Service and Traffic Impacts Continued

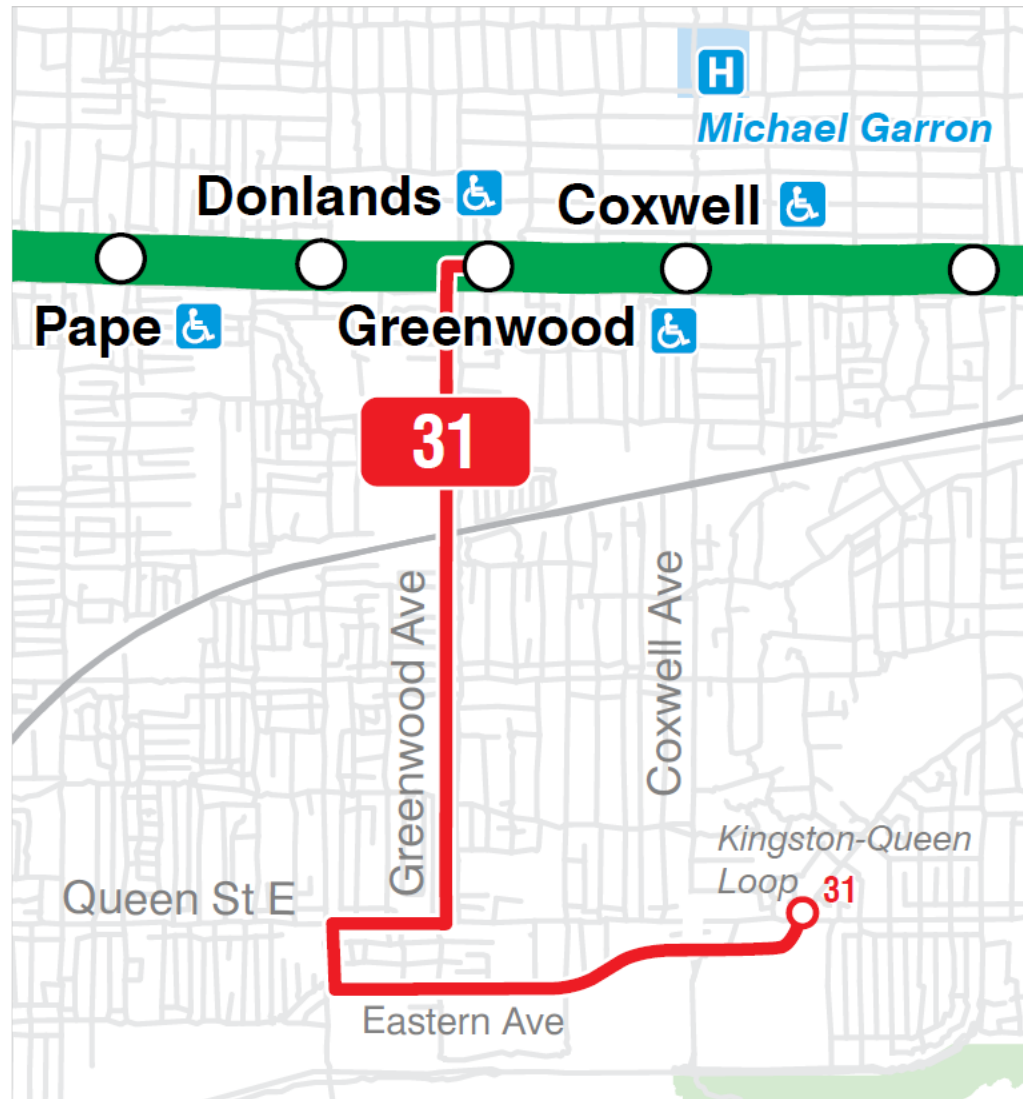

Bus #31 resumed regular service at the Station's bus loop for customer drop-off and pick-up on February 10, 2026.

Wayfinding signage is in place to direct customers accordingly.

31 Greenwood route map

| Construction

- The majority of work will take place between 7 a.m. and 7 p.m., as required.
- As permitted, some overnight and weekend work will be required during the course of this project in order to complete the work as quickly as possible.
- Noise, dust and vibration associated with construction is unavoidable with this work.
- Mitigation measures such as vibration monitoring, and mesh fencing (to reduce dust) is implemented.
- Construction trucks, equipment and workers are present in the general area.
- TTC Community Liaison will provide construction updates, coordinate responses to questions, coordinate meetings with neighbours and the project team.

| The Danforth and Local Businesses

- Please note that this project does not take place on the Danforth.
- The laneway north of the Danforth will remain open and available. The laneway itself is under the City's jurisdiction. Please call 311 for any laneway concerns related to traffic, encroachment, maintenance and salting/snow removal.
- Area waste collection conducted by the City will continue as per their schedule.



| Greenwood Station Public Art

- Greenwood Station will receive public art in accordance with the TTC Public Art Policy.
- An open call and pre-qualification will be issued; three artists will be selected per station to create and present an art concept.
- A jury from the Arts community will be formed including a member with ties to the neighbourhood.
- Art will be installed at a later date (TBD).

